

JLK INSPECTION 281.344.2444

info@JLKinspect.com https://www.JLKInspect.com



INSPECTION REPORT

1234 Main Street Katy TX 77494

> Buyer Name 07/08/2023 9:00AM



Inspector
JUSITN JOSEPH
TREC #25938
281.344.2444
info@JLKinspect.com



Agent Name 555-555-5555 agent@spectora.com



PROPERTY INSPECTION REPORT FORM

Buyer Name Name of Client 1234 Katy TX 77494	07/08/2023 9:00AM Date of Inspection		
Address of Inspected Property			
JUSITN JOSEPH	TREC #25938		
Name of Inspector	TREC License #		
Justin Joseph, TREC # Name of Sponsor (if applicable)	25938 TREC License #		

PURPOSE OF INSPECTION

A real estate inspection is a visual survey of a structure and a basic performance evaluation of the systems and components of a building. It provides information regarding the general condition of a residence at the time the inspection was conducted. *It is important* that you carefully read ALL of this information. Ask the inspector to clarify any items or comments that are unclear.

RESPONSIBILITY OF THE INSPECTOR

This inspection is governed by the Texas Real Estate Commission (TREC) Standards of Practice (SOPs), which dictates the minimum requirements for a real estate inspection.

The inspector IS required to:

- use this Property Inspection Report form for the inspection;
- inspect only those components and conditions that are present, visible, and accessible at the time of the inspection;
- indicate whether each item was inspected, not inspected, or not present;
- indicate an item as Deficient (D) if a condition exists that adversely and materially affects the performance of a system or component **OR** constitutes a hazard to life, limb or property as specified by the SOPs; and
- explain the inspector's findings in the corresponding section in the body of the report form.

The inspector IS NOT required to:

- identify all potential hazards;
- turn on decommissioned equipment, systems, utilities, or apply an open flame or light a pilot to operate any appliance;
- climb over obstacles, move furnishings or stored items;
- prioritize or emphasize the importance of one deficiency over another;
- provide follow-up services to verify that proper repairs have been made; or
- inspect system or component listed under the optional section of the SOPs (22 TAC 535.233).

RESPONSIBILTY OF THE CLIENT

While items identified as Deficient (D) in an inspection report DO NOT obligate any party to make repairs or take other actions, in the event that any further evaluations are needed, it is the responsibility of the client to obtain further evaluations and/or cost estimates from qualified service professionals regarding any items reported as Deficient (D). It is recommended that any further evaluations and/or cost estimates take place prior to the expiration of any contractual time limitations, such as option periods.

Please Note: Evaluations performed by service professionals in response to items reported as Deficient (D) on the report may lead to the discovery of additional deficiencies that were not present, visible, or accessible at the time of the inspection. Any repairs made after the date of the inspection may render information contained in this report obsolete or invalid.

REPORT LIMITATIONS

This report is provided for the benefit of the named client and is based on observations made by the named inspector on the date the inspection was performed (indicated above).

ONLY those items specifically noted as being inspected on the report were inspected.

This inspection IS NOT:

- a technically exhaustive inspection of the structure, its systems, or its components and may not reveal all deficiencies;
- an inspection to verify compliance with any building codes;
- an inspection to verify compliance with manufacturer's installation instructions for any system or component and DOES NOT imply insurability or warrantability of the structure or its components.

NOTICE CONCERNING HAZARDOUS CONDITIONS, DEFICIENCIES, AND CONTRACTUAL AGREEMENTS

Conditions may be present in your home that did not violate building codes or common practices in effect when the home was constructed but are considered hazardous by today's standards. Such conditions that were part of the home prior to the adoption of any current codes prohibiting them may not be required to be updated to meet current code requirements. However, if it can be reasonably determined that they are present at the time of the inspection, the potential for injury or property loss from these conditions is significant enough to require inspectors to report them as Deficient (D). Examples of such hazardous conditions include:

- malfunctioning, improperly installed, or missing ground fault circuit protection (GFCI) devices and arc-fault (AFCI) devices;
- ordinary glass in locations where modern construction techniques call for safety glass;
- malfunctioning or lack of fire safety features such as smoke alarms, fire-rated doors in certain locations, and functional emergency escape and rescue openings in bedrooms;
- malfunctioning carbon monoxide alarms;
- excessive spacing between balusters on stairways and porches;
- improperly installed appliances;
- improperly installed or defective safety devices;
- lack of electrical bonding and grounding; and
- lack of bonding on gas piping, including corrugated stainless steel tubing (CSST).

Please Note: items identified as Deficient (D) in an inspection report DO NOT obligate any party to make repairs or take other actions. The decision to correct a hazard or any deficiency identified in an inspection report is left up to the parties to the contract for the sale or purchase of the home.

This property inspection report may include an inspection agreement (contract), addenda, and other information related to property conditions.

INFORMATION INCLUDED UNDER "ADDITIONAL INFORMATION PROVIDED BY INSPECTOR", OR PROVIDED AS AN ATTACHMENT WITH THE STANDARD FORM, IS NOT REQUIRED BY THE COMMISSION AND MAY CONTAIN CONTRACTUAL TERMS BETWEEN THE INSPECTOR AND YOU, AS THE CLIENT. THE COMMISSION DOES NOT REGULATE CONTRACTUAL TERMS BETWEEN PARTIES. IF YOU DO NOT UNDERSTAND THE EFFECT OF ANY CONTRACTUAL TERM CONTAINED IN THIS SECTION OR ANY ATTACHMENTS, CONSULT AN ATTORNEY.

ADDITIONAL INFORMATION PROVIDED BY INSPECTOR

In Attendance: Buyer Occupancy: Vacant Style: Modern

Temperature (approximate): 86 Fahrenheit (F)

Type of Building: Single Family Weather Conditions: Clear

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

NI NP D

I. STRUCTURAL SYSTEMS

☒ □ □ □ A. Foundations

Type of Foundation(s): Monolithic Style Slab On Grade

Foundation Statement:

The foundation appeared to be in functional condition with no major signs of movement or settlement.

Buyers Advisory Notice:

These opinions are based solely on the observations of the inspector which were made without sophisticated testing procedures, specialized tools and/or equipment. Therefore the opinions expressed are of apparent conditions and not absolute fact and are only good on 05/06/2023.

Comments:

1: Slab - Corner Crack/Pop

Recommendation

One or more of the foundation perimeter beams were observed to be cracked or sheared off. This is a common condition in slab-on-grade foundations. This condition does not adversely affect the performance of the foundation. However, in some cases, some cosmetic improvements may be necessary




I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D

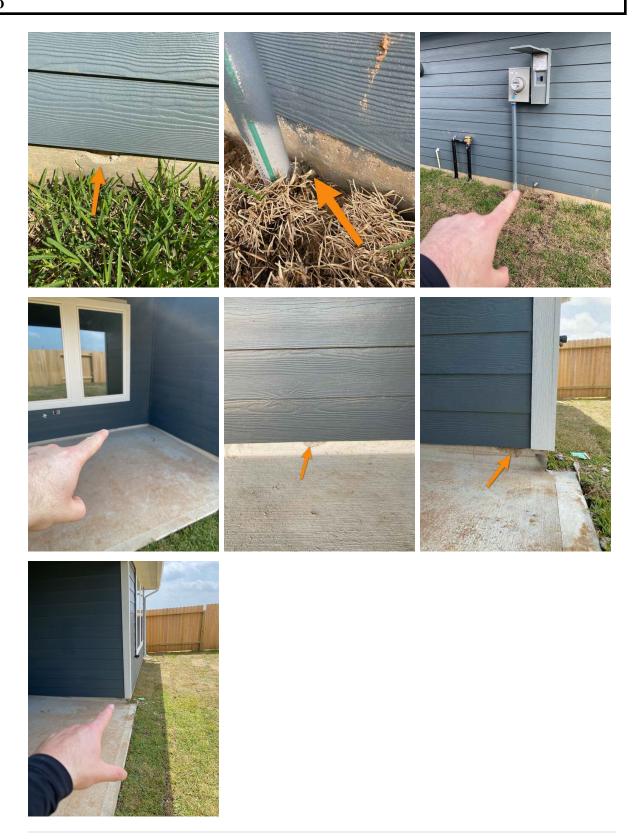

2: Metal bracket

I=Inspected

NI=Not Inspected **NP=Not Present D=Deficient**

NI NP D

*Recommend Maintenance

Metal bracket was observed at the rear patio door. Recommend removal.

Recommendation: Contact a qualified professional.



X B. Grading and Drainage

Gutters & Downspouts Material: Metal Comments:

1: Missing downspout kick-out or extension

Recommendation

A missing downspout kick-out(s) or extension(s) was observed. Downspouts should discharge at least 5 feet away from the foundation; if not corrected, this could cause foundation issues. Recommend installing or extending out from the foundation.

Recommendation: Contact a handyman or DIY project



I=Inspected NI=Not Inspected NP=Not Present D=Deficient

NI NP D

☑ □ □ ☑ C. Roof Covering Materials

Roof Type: Gable, Hip & Valley

Types of Roof Covering: Asphalt Composition Shingle - Architectural





Viewed From: Roof Number of Layers: 1

Vent Penetrations: Plumbing Vents, Heating Vents

Flashing Material: Metal Skylight Types: Not Installed

Comments:

1: Roof – Racking shingles

Recommendation

Racking shingle was observed at the right and rear of the roof. Recommend correcting.


I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D

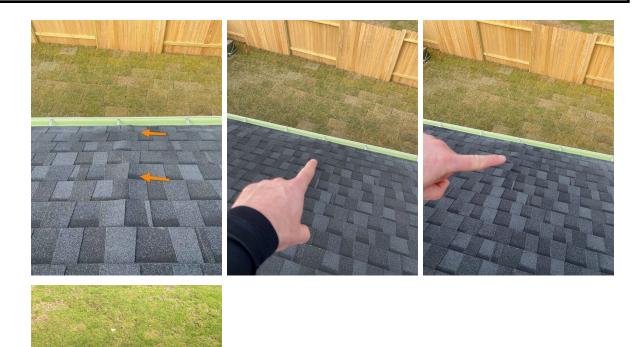

☑ □ □ ☑ D. Roof Structures and Attics

Viewed From: Partially Accessed - Due to Insulation

Access Location: Garage

Approximate Average Depth of Insulation: 13 Inches

Roof & Ceiling Structure: Rafters (2x6), Ceiling Joists (2x6)

Sheathing Type: Radiant Barrier - O.S.B. *Insulation Type:* Loose Fill - Fiberglass

Vapor Retarder: Not Installed Air Ventilation Type: Eave, Hooded

Attic Fan: Not Installed

Comments:

Partially Accessed - Due to Insulation:

A limited review of the attic was due to loose fill insulation covering the framing. The inspector did not disturb the insulation to traverse the ceiling joist. Suggest verifying the overall condition before the end of the contingency period.

1: Loose framing member

I=Inspected NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D

Recommendation

A loose framing member was observed in the attic near the furnace. Recommend correcting.

Recommendation: Contact a qualified professional.



X E. Walls (Interior and Exterior)

Interior Wall Cladding: Drywall/Sheetrock Exterior Wall Cladding: Concrete Composition Comments:

1: Exterior - Siding Holes

Recommendation

Unsealed holes were observed at the exterior wall cladding. Recommend repair.



2: Exterior - Siding Clearance to Grade

resport functions. 123 i Main Surest Raty 171 // 151 05/30/2021

I=Inspected NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D

Recommendation

Inadequate clearance was observed between the wall cladding and the grade. Recommend correcting.

Recommendation: Contact a qualified Grading/Drainage Contractor



3: Exterior - Trim voids

Recommendation


The window trim was incorrectly installed; it observed all the windows. Recommend correcting.



NP=Not Present I=Inspected NI=Not Inspected **D=Deficient**

NI NP D





4: Exterior - Deteriorated caulking

Recommendation

Deteriorated/missing caulking was observed in a number of areas on the exterior. Recommend caulking.

Recommendation: Contact a qualified professional.



5: Exterior – Overdriven siding nails

Recommendation

Overdriven siding nails were observed on the right side near the rear fence. Recommend correcting.

I=Inspected

NP=Not Present NI=Not Inspected

D=Deficient

NI NP D





 \mathbf{X} F. Ceilings and Floors Comments: X **G. Doors (Interior and Exterior)** Comments: H. Windows X Comments: \mathbf{X} I. Stairways (Interior and Exterior) Comments: \mathbf{X} J. Fireplaces and Chimneys Comments:

Report Identification: 1234 Main Street Katy TX 77494 - 09/30/2021

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

M Carports

Comments:

Page 12 of 23

I=Inspected

NI=Not Inspected **NP=Not Present** **D=Deficient**

NI NP D

II. ELECTRICAL SYSTEMS

A. Service Entrance and Panels

Electrical Service Entrance: Below Ground









Main Disconnect Amperage: 125 amp Main Disconnect Location: Left side Main Disconnect Manufacturer: Square D Sub Panel Disconnect Location: Garage Sub Panel Disconnect Manufacturer: Square D

Comments:

B. Branch Circuits, Connected Devices, and Fixtures

Type of Wiring: Copper Comments:

1: Light Switch Use (Interior)

*Recommend Maintenance

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

NI NP D

Unable to determine use for light switch at the guest bedrooms.

Recommendation: Contact a qualified professional.





2: Fixture - Missing lightbulb

*Recommend Maintenance

Missing lightbulb was observed in the attic. Recommend installing.

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

NI NP D



□ □ ☑ □ C. Other

Comments:

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

NI NP D

III. HEATING, VENTILATION AND AIR CONDITIONING SYSTEMS

☒ □ □ **□** A. Heating Equipment

Type of Systems: Gas-Fired Heat





Energy Sources: Gas

Comments:

☑ □ □ ☑ B. Cooling Equipment

Type of Systems: Central Air Conditioner







Comments:

1: Unit Not Level

Recommendation

Concrete pad supporting the outdoor condensing unit is not level. This can cause accelerated deterioration of components. Recommend licensed HVAC contractor level the unit.

I=Inspected NI=Not Inspected NP=Not Present **D=Deficient**

NI NP D



C. Duct Systems, Chases, and Vents

Comments:

 X D. Other

Comments:

Limited review - fresh air controller:

A fresh air venting system was observed in the attic. This is beyond the inspection scope.





I=Inspected NI=Not Inspected

NI

NP=Not Present

D=Deficient

NP D

IV. PLUMBING SYSTEMS

 \mathbf{X} A. Plumbing Supply, Distribution Systems, and Fixtures

> Location of Water Meter: Exterior Location of Main Water Supply Valve: Garage



Static Water Pressure Reading: 60



Type of Supply Piping Material: PEX Comments:

1: Meter - Flooded Crock

Recommendation

Water meter crock was flooded at time of inspection. Recommend further review by a qualified plumber, prior to the end of the contingency period.

I=Inspected NI=Not Inspected

D

NP=Not Present

D=Deficient

NI NP



\mathbf{X} B. Drains, Wastes, and Vents

Type of Drain Piping Material: ABS Comments:

1: Sewer clean out clogged

Recommendation

Standing water was observed at the sewer cleanout. Recommend further review by qualified plumber prior to the end of the contingency.







I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D



🛛 🗆 🗖 🖒 C. Water Heating Equipment

Energy Sources: Gas Comments:

1: Condensation line missing

Recommendation

Exhaust vent condensation line was not installed. Recommend installing with a neutralizing filter.

Recommendation: Contact a qualified professional.





□ □ **B** □ **D.** Hydro-Massage Therapy Equipment

Comments:

☑ □ □ □ E. Gas Distribution Systems and Gas Appliances

Location of Gas Meter: Right side

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

NI NP D



Type of Gas Distribution Piping Material: Cast Iron *Comments:*

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

1	111	NP	<u> </u>	
				V. APPLIANCES
×				A. Dishwashers Comments:
×			×	B. Food Waste Disposers Comments:
				1: Splash guard Recommend Maintenance
				Splash guard is damaged/missing. Suggest repair. Recommendation: Contact a qualified professional.
×				C. Range Hood and Exhaust Systems Comments:
×				D. Ranges, Cooktops, and Ovens Comments:
×				E. Microwave Ovens Comments:
×				F. Mechanical Exhaust Vents and Bathroom Heaters Comments:
×				G. Garage Door Operators Comments:
×				H. Dryer Exhaust Systems Comments:

I=Inspected NI=Not Inspected

NI NP D NP=Not Present

D=Deficient

VI. OPTIONAL SYSTEMS

 \mathbf{X} A. Landscape Irrigation (Sprinkler) Systems

Comments:

1: Exposed low-voltage wires

Recommendation

Expose low-voltage wires observed. Recommend correcting.



